

Review Article

AN ANALYSIS OF EFFECTS OF MONITORING AND EVALUATION PRACTICES ON THE IMPLEMENTATION OF EDUCATIONAL PROJECTS AMONG NON-GOVERNMENTAL ORGANIZATIONS IN KAKUMA REFUGEE CAMP KENYA .

Abstract

A significant challenge facing NGO-funded educational projects in Kenya is the lack of access to quality educational resources and infrastructure. Despite efforts to provide education to needy populations, many schools in the lack basic facilities such as classrooms, textbooks, and teaching materials. This study examined how monitoring and evaluation (M&E) practices impact the effective execution of education projects by NGOs operating in Kakuma refugee camp. It aimed to achieve four main objectives related to M&E: assessing the influence of M&E planning, evaluating M&E technical expertise, understanding management participation's role, and exploring stakeholder involvement. Drawing insights from systems management theory, program theory, and stakeholder theory, the research employed a descriptive survey design focusing on nine NGOs under UNHCR supporting education initiatives in Kakuma refugee camp. Both closed and open-ended questionnaires were used, with a pilot study ensuring questionnaire validity. Data analysis involved employing SPSS version 22, with statistical techniques including frequency distribution tables and Cronbach's alpha for reliability. The study highlighted the crucial role of comprehensive M&E planning, technical expertise, management participation, and stakeholder engagement in project success. While positive perceptions and significant correlations were observed, improvements are necessary, particularly in enhancing community involvement and continuous improvement efforts. It's recommended to prioritize addressing these areas to optimize project outcomes within the camp.

Key Words: Planning, technical expertise, management participation, stakeholder engagement in refugee camp kakuma, kenya.

Introduction

Non-Governmental Organizations (NGOs) are established with defined goals and objectives, implementing clear plans and monitoring mechanisms to achieve them (Jardioui et al., 2020). Effective monitoring and evaluation (M&E) practices, a common strategy, are crucial for organizations to reach their targets and ensure prudent resource utilization for desirable financial

performance (Abongo, 2018; Vernimmen et al., 2022). M&E practices involve various activities such as engaging stakeholders, building capacity, planning, and managing data, all contributing to project learning, decision-making, and ultimately project performance (Scheirer, 2018). Kusek and Rist (2019) affirm that both monitoring and evaluation entail effective practices, including implementing a participative approach, aligning the M&E strategy with the work plan and strategic plan, sharing M&E findings with stakeholders, and utilizing M&E data to enhance the project.

According to the Kenya Comprehensive Refugee Programme (2016), the Kakuma Refugee Camp opened in 1992 and is one of Kenya's largest refugee camps, with around 158,000 people. Kakuma Refugee Camp is home to around twenty-four non-governmental organisations (NGOs). Of these, nine are directly involved with educational issues. The coordination of the NGOs is regulated by UNHCR, which is the entity empowered to oversee the operations of the other NGOs working in the camp. Although UNHCR provides the majority of the finances, other partners also give matching funds to their budget to satisfy the needs of the refugees and the surrounding population within Kakuma (UNHCR, 2023). These NGOs are instrumental in providing access to formal and informal educational opportunities for refugees, with a focus on enhancing literacy, numeracy, and vocational skills. Through the implementation of schools, learning centers, and community-based initiatives, these programs contribute to empowering individuals, particularly children and youth, by fostering resilience and facilitating a sense of normalcy in the midst of difficult circumstances (UNHCR, 2023). NGOs often collaborate with local communities, leveraging innovative teaching methods and culturally sensitive approaches to cater to the diverse needs of the refugee population with aim to break the cycle of poverty and

displacement by equipping refugees with the tools necessary for a more secure and hopeful future.

Specific Objectives of the Study

- To determine how planning for M&E influence implementation of educational projects among NGOs in Kakuma refugee camp in Kenya.
- To establish the influence of M&E technical expertise on implementation of educational projects among NGOs in Kakuma refugee camp in Kenya.
- To assess how management participation in M&E influence implementation of educational projects among NGOs in Kakuma refugee camp in Kenya.
- To establish the influence of stakeholder involvement on implementation of educational projects among NGOs in Kakuma refugee camp in Kenya.

2.0 Literature Review

The study was guided by the following theories: the systems management theory, program theory and stakeholder theory.

3.0 Conceptual Frame work

A conceptual framework serves as a theoretical framework that outlines the connections between independent, intervening, and dependent variables within a research study. Functioning as a guide, it visually represents the hypothesized relationships and directs the overall research design (Peeters, Krahmer & Maes, 2021).

Independent Variable

Moderating Variable

Dependent Variable

Independent Variable

Moderating Variable

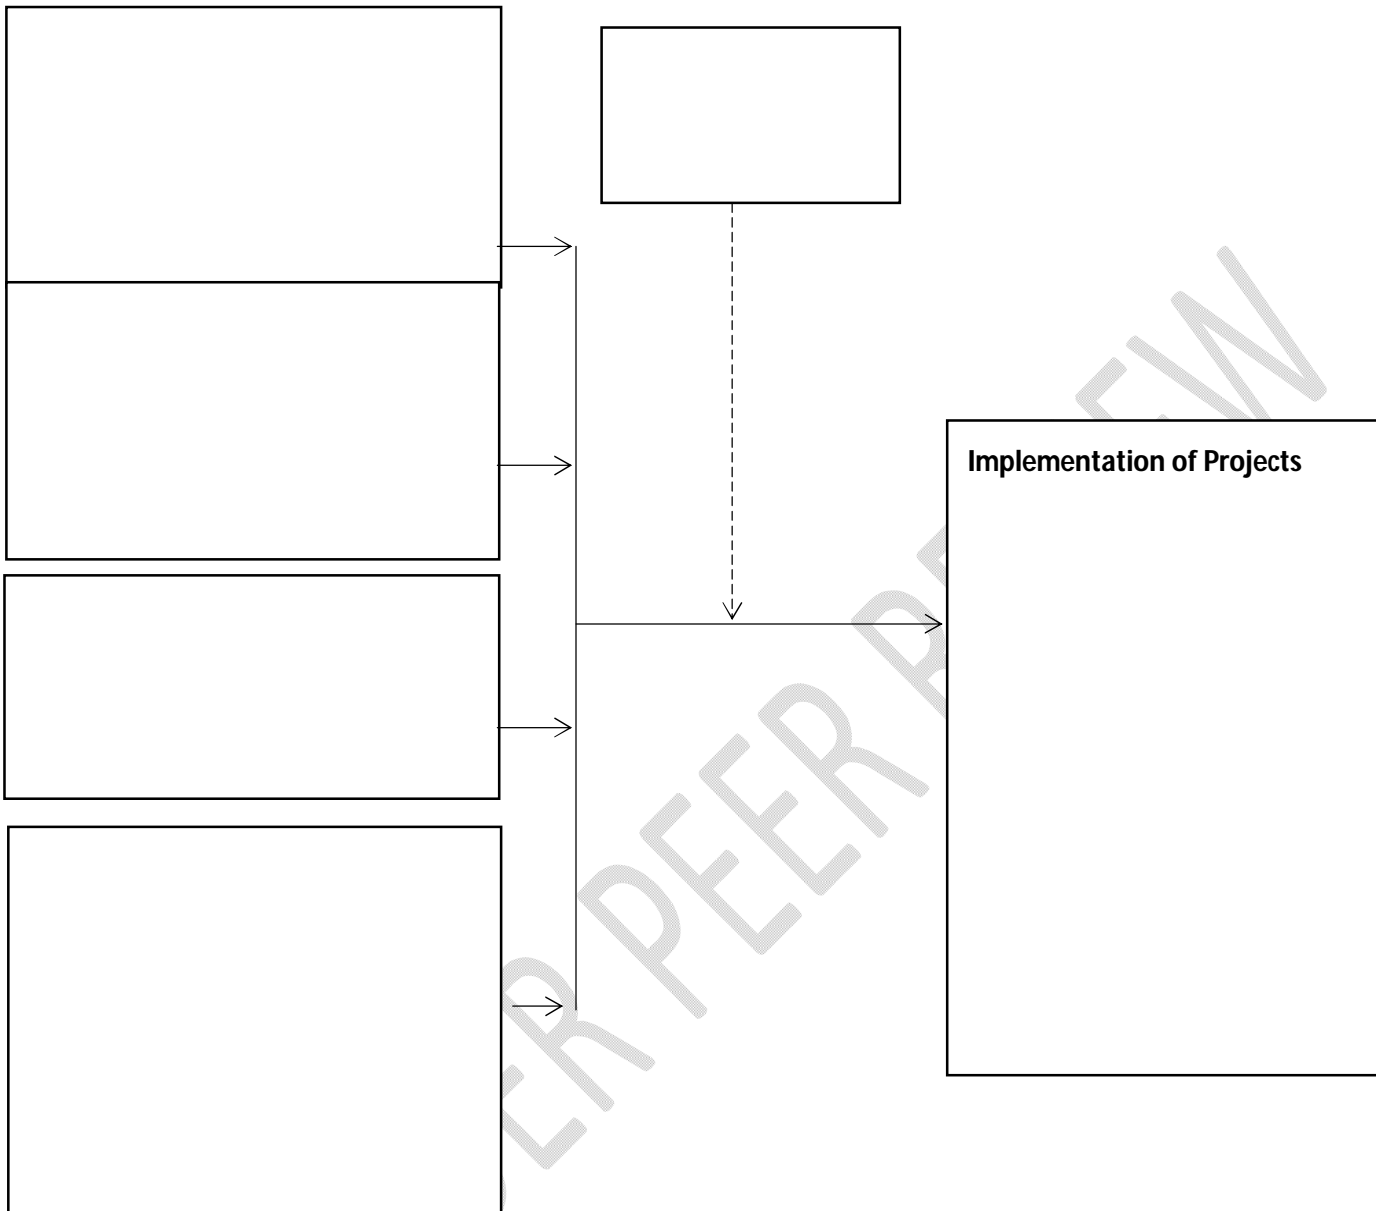


Figure 1: Conceptual Framework
Source: Researcher (2024)

Effects of monitoring & Evaluation Planning on Project Implementation in kakuma refugee camp, Kenya.

A study conducted in 2021 by Kadel, Ahmad, and Bhattarai focused on highlighting the strategies that should be used to improve planning, M&E, and efficacy. The study found that

M&E significantly depends on clear and concise planning as well as a clear understanding of what has to be monitored through the use of the desk review approach. The creation of the monitoring and evaluation activity plan and the creation of the indicator reference sheet were found to be the primary priorities during the M&E planning process. The features of M&E planning that were discussed included timeliness, progress tracking, reporting on a regular basis, and mid- and end-term reviews. Analytical techniques such as factor, correlation, and factor analysis were used to produce evidence.

Effects of M&E Technical Expertise on Project Implementation in Kakuma refugee camp, Kenya.

Technical competencies are the abilities necessary for monitoring and evaluating procedures, necessitating a foundational education in M&E for practitioners. Its cost, standards, acceptability, suitability, and responsiveness are its main determinants. Oday (2021) conducted study on project implementation expertise in Fiji. A survey-based descriptive research design was employed in the study. A field survey employing questionnaires served as the primary data source, and previously published materials such as books and journals served as the secondary source. The findings indicate that most projects were managed through appropriate organisational frameworks, which led to a focus on achieving goals at the expense of the human resource that is essential to any project's success. Their research had a conceptual gap because it was centred on a distinct setting. The current study focused on effects of technical expertise on project implementation in Kenya.

Effects of Management Participation on Project Implementation in Kakuma refugee camp, Kenya.

The study found out that the active involvement of management in decision-making processes, resource allocation, and problem-solving contributes to the overall efficiency of project implementation. Management participation facilitates clear communication channels, aligns project objectives with organizational goals, and enhances the understanding of project requirements among team members. This involvement is particularly vital in the construction industry, where complex and dynamic environments require timely and informed decision-making. When top management actively engages in the M&E process, it demonstrates a commitment to project success and encourages a sense of responsibility throughout the organization. Their oversight provides strategic direction, enabling quick decision-making and adjustments as needed.

Impact of Stakeholder Participation on Project Implementation in kakuma Refugee camp, Kenya

Nederhand and Klijn (2019) pinpointed four significant potential benefits of engaging essential stakeholders like employees and proprietors in managerial processes. When employees are actively engaged in shaping and progressing the company's vision, they are more likely to endorse forthcoming changes associated with it. Additionally, when workers, clients, and investors participate, they unearth diverse problem-solving approaches. When someone is involved in proposing solutions, they foster a sense of allegiance to the management because they feel appreciated within the organization due to their contributions. The choice of approach for stakeholder management was often influenced by project characteristics and stakeholder attributes, with a preference for standardized methodologies.

Impact of government Policies on Project Implementation in kakuma refugee camp, Kenya.

Taylor and Garcia (2017) focused their investigation on the role of government legislation in a detailed analysis of the external elements defining the environment for women's table banking self-help groups. Their findings highlighted the vital need for regulatory frameworks that enable and improve these organizations' functioning. Miller and Anderson (2018) expand on this viewpoint by delving into the complex interaction between the political climate and the distribution of resources and support for government projects. Their research illuminates the dynamic interplay between politics and resource distribution, highlighting the importance of the larger political backdrop in determining the terrain for these efforts.

3.0 Research Methodology

3.1. Research Design

The utilization of a descriptive survey design allowed the researcher to measure Monitoring and Evaluation (M&E) through the use of questionnaires, establishing a connection between M&E and the execution of educational projects. The survey approach enabled the collection of information on M&E and project implementation without manipulating the variables.

3.3 Study Area

This study was carried out in Kakuma refugee camp located in Turkana County in northwestern Kenya.

3.4 Target Population

The research focused on 9 NGOs under UNHCR that support education programs in Kakuma refugee camp. According to UNHCR (2024), the nine NGOs has a total of 143 official staff who took part in this research study. The research encompassed a diverse group of professionals within the nine NGOs under UNHCR that actively support education programs in Kakuma

refugee camp. These included project managers, teachers and educators, social workers, administrative staff, health professionals, contributing to the health and wellness aspects of education programs; community liaison officers, monitoring and evaluation specialists, program coordinators, and support staff. The inclusion of these diverse professionals aimed at capturing a comprehensive understanding of the educational initiatives and their multifaceted impacts on the refugee community in Kakuma.

Table 1: Target Population

| Category Target Population (N) | |
|---------------------------------------|------------|
| Administrative staff | 20 |
| Community Liaison officers | 18 |
| Health Professionals | 10 |
| Monitoring and Evaluation Staff | 15 |
| Program Coordinators | 10 |
| Project Managers | 25 |
| Social workers | 15 |
| Support Staff | 10 |
| Teachers | 40 |
| Total | 143 |

Source: UNHCR (2024)

3.5 Sample and Sampling Technique

The research utilized a census sampling technique and selected all the 143 respondents. Census sampling enables the collection of detailed and comprehensive information from each respondent. This approach allows for an in-depth understanding of the experiences, challenges, and successes of these individuals, contributing to a rich and detailed analysis.

Table 2: Sample Size

| Category Sample Size (S) | |
|---------------------------------|------------|
| Administrative staff | 20 |
| Community Liaison officers | 18 |
| Health Professionals | 10 |
| Monitoring and Evaluation Staff | 15 |
| Program Coordinators | 10 |
| Project Managers | 25 |
| Social workers | 15 |
| Support Staff | 10 |
| Teachers | 40 |
| Total | 143 |

3.6 Data collection methods and procedures

The study employed both close ended and open ended questionnaires. The close ended instrument had two sections. The demographic characteristics of the respondents and the second part had the questions from the four independent variables in relation to dependent variable. The survey instrument was disseminated through the drop and pick method, a practical approach chosen for its convenience and flexibility. Printed questionnaires, accompanied by envelopes containing clear instructions, were distributed to the participants

at their respective locations. A designated drop-off point was communicated, allowing participants to complete the questionnaires at their convenience. Once completed, participants sealed the questionnaires in the provided envelopes and dropped them off at the specified location for subsequent collection.

3.7.1 Validity of the Research Instruments

The validity of the questionnaire was ensured through test and retest process. Content validity was established by conducting a thorough review of existing literature, consulting subject matter experts and aligning the questionnaire with the research objectives and conceptual framework. Content validity was utilized to ensure simplicity and clarity by simplifying the instruments and using clear language in questions, ensuring participant familiarity and comprehension.

3.7.2 Reliability of Instruments

The piloted outcomes were assessed to determine if they yielded reasonably comparable results. The calculation of the reliability index utilized Cronbach's alpha, and this analysis followed the descriptive statistics of individual variables. The created scale is more dependable with a higher score. According to Taber (2018), a reliability of 0.7 is considered acceptable, hence deemed sufficient for this investigation.

3.8 Data Analysis and Presentation

This is the process of inspecting, cleaning, transforming, and modeling data to discover useful information, draw conclusions, and support decision-making. Quantifiable forms were created from qualitative data. Software called SPSS version 22 was used to analyze the data that was obtained quantitatively. Each variable's estimated statistic was recorded in a frequency distribution table. By using descriptive statistics measures of central tendency and dispersion

Table 3; M&E Planning in Implementation of education projects among NGOs in Kakuma refugee camp

N=121

The study results on M&E Planning and implementation of education projects among NGOs in Kakuma refugee camp are displayed in Table 4. The first construct sought whether M&E plans associated with the projects are comprehensive and cover all relevant aspects. Most respondents agreed with the statement (Mean=4.26, SD=.624). The second construct sought whether quality indicators are adequately addressed in our M&E plans, ensuring the delivery of high-quality project outcomes. Most respondents agreed with the statement (Mean=3.99, SD=.681). Lastly, most participants agreed that financial aspects are well-integrated into our M&E plans, facilitating efficient budgeting and resource allocation (Mean=3.94, SD=.708). Overall, the composite mean for all components was 4.06, reflecting a high overall perception of M&E planning activities undertaken by different educational NGOs at Kakuma refugee camp.

Correlation Analysis

The coefficient of Pearson's correlation was used by the researcher to show how M&E Planning and implementation of education projects are related.

| Variable | | M&E Planning | Implementation of education projects among NGOs in Kakuma refugee camp |
|--------------|---------------------|--------------|--|
| M&E Planning | Pearson Correlation | 1 | 0.812** |
| | Sig. (2-tailed) | | 0.000 |
| | n | 121 | 121 |

| | | | |
|--|---------------------|---------|-----|
| Implementation of education projects among NGOs in Kakuma refugee camp | Pearson Correlation | 0.812** | 1 |
| | Sig. (2-tailed) | 0.000 | |
| | n | 121 | 121 |
| **. Correlation is significant at the 0.05 level (2-tailed). | | | |

Table 4; Correlation Analysis between M&E Planning and Implementation of education projects

The correlation analysis in Table 4 indicates a strong positive correlation ($r = 0.812$, $p = 0.000$) between M&E Planning and implementation of education projects among NGOs in Kakuma refugee camp. The 0.812 coefficient shows a robust positive association between these variables. These findings agrees with a number of studies.

Regression Analysis

This was to show the connection of M&E Planning to the implementation of education projects among NGOs in Kakuma refugee camp. Simple linear regression was utilized.

| Model | R | R Square | Adjusted R Square | Std. Error of the Estimate |
|---|-------------------|----------|-------------------|----------------------------|
| 1 | .812 ^a | .710 | .634 | .4861 |
| a. Predictors: (Constant), M&E Planning | | | | |

Table 5; Model Summary for M&E Planning and implementation of education projects

Table 5 delves into the link between M&E Planning and the implementation of education projects among NGOs in Kakuma refugee camp through a simple linear regression model. The results highlight M&E Planning as a significant predictor of implementation of education projects. The R Square value of 0.710 indicates that 71% of the variance in success in implementation of education projects can be explained by variations in M&E Planning. The

N=121

Table 6; M&E Technical expertise and Implementation of education projects

This objective aimed to investigate how M&E Technical expertise influences the implementation of education projects among NGOs in Kakuma refugee camp. Table 7 illuminates the impact of M&E Technical expertise. The first statement, sought whether personnel involved in M&E activities receive adequate training to effectively carry out their roles. From the findings, majority of the respondents agreed with the statement (Mean=4.31, SD=.613). The second construct sought whether the level of experience within our M&E team is sufficient to handle diverse projects and challenges (Mean=4.44, SD=.595). From the statistics, majority of the respondents strongly agreed with the statement. Lastly, the study sought whether organizations prioritizes and actively engages in continuous improvement initiatives related to M&E processes. Most respondents disagreed with the statement (Mean=2.52, SD=.812). Overall, the composite mean for all components is 3.76, reflecting a positive perception of M&E Technical expertise for educational NGOs at Kakuma refugee camp.

Correlation Analysis

The coefficient of Pearson correlation was used to demonstrate the relationship between M&E Technical expertise and the implementation of education projects among NGOs in Kakuma refugee camp.

| Variable | | M&E Technical expertise | Implementation of education projects among NGOs in Kakuma refugee camp |
|-------------------------|---------------------|-------------------------|--|
| M&E Technical expertise | Pearson Correlation | 1 | 0.630** |

| | | | |
|--|---------------------|---------|-------|
| | Sig. (2-tailed) | | 0.000 |
| | n | 121 | 121 |
| Implementation of education projects among NGOs in Kakuma refugee camp | Pearson Correlation | 0.630** | 1 |
| | Sig. (2-tailed) | 0.000 | |
| | n | 121 | 121 |

Table 7; Correlation Analysis

In Table 7, the correlation analysis shows a strong positive correlation ($r = 0.630$, $p = 0.000$) between M&E Technical expertise and the implementation of education projects among NGOs in Kakuma refugee camp. With a coefficient of 0.630, the variables are strongly positively associated. These findings agree with a number of studies.

Regression Analysis

This was conducted to establish the association between M&E Technical expertise and the implementation of education projects among NGOs in Kakuma refugee camp. Simple linear regression was utilized.

| Model | R | R Square | Adjusted R Square | Std. Error of the Estimate |
|--|-------------------|----------|-------------------|----------------------------|
| 1 | .630 ^a | .553 | .482 | .4711 |
| a. Predictors: (Constant), M&E Technical expertise | | | | |

Table 8; Model Summary of Resource allocation and implementation of education projects among NGOs in Kakuma refugee camp

In the regression analysis (Table 8), M&E Technical expertise emerged as a crucial predictor of success in implementation of education projects among NGOs in Kakuma refugee camp. About 55.3% of the variance in success is explained by variations in M&E Technical expertise (R

Square = 0.553). Considering model complexity, the Adjusted R Square is 0.482, signifying that approximately 48.2% of the variance is explained by M&E Technical expertise. The positive correlation coefficient ($R = 0.630$) underlines a robust positive relationship between M&E Technical expertise and the implementation of education projects among NGOs in Kakuma refugee camp.

Additionally, an ANOVA test was performed to determine the significance of M&E Technical expertise as an indicator of the implementation of education projects among NGOs in Kakuma refugee camp.

| Model | | Sum of Squares | df | Mean Square | F | Sig. |
|-------|------------|----------------|-----|-------------|---------|-------------------|
| 1 | Regression | 78.237 | 1 | 78.237 | 102.223 | .000 ^b |
| | Residual | 111.234 | 120 | .480 | | |
| | Total | 189.471 | 121 | | | |

Table 9; ANOVA of M&E Technical expertise and implementation of education projects

Table 9 shows that M&E Technical expertise has a considerable impact on the implementation of education projects among NGOs in Kakuma refugee camp and is a significant predictor, with $[F(1, 120) = 102.223, P.05]$.

Influence of management participation on Implementation of education projects among NGOs in Kakuma refugee camp

This third objective sought to establish the impact of management participation on the implementation of education projects among NGOs in Kakuma refugee camp. Three opinion statements were provided, and answers were recorded on a five-point scale range from strongly disagree (1) to strongly agree (5). Table 9 shows the results.

| STATEMENTS | 1 | 2 | 3 | 4 | 5 | Mean | Std. Dev. |
|--|-----|-------|-------|-------|-------|-------------|--------------|
| Senior management demonstrates a strong commitment to the success of projects and initiatives. | 10% | 12.3% | 9.7% | 43% | 25% | 4.18 | 0.671 |
| There is effective and transparent communication between management and project teams. | 10% | 15.3% | 15.3% | 37.3% | 22.1% | 3.82 | 0.745 |
| The organizational culture promotes and supports active participation and collaboration from management in project activities. | 11% | 14.7% | 10.3% | 37.3% | 26.7% | 3.95 | 0.722 |
| Composite mean and SD | | | | | | 3.98 | 0.713 |

Table 10; Influence of management participation on implementation of education projects among NGOs in Kakuma refugee camp

N=121

Table 10 displays the study's findings on Influence of management participation and their impacts on the implementation of education projects among NGOs in Kakuma refugee camp. The majority of participants agreed with the first construct that senior management demonstrates a strong commitment to the success of projects and initiatives. (Mean=4.18, SD=.671). Majority of the respondents also agreed that there is effective and transparent communication between management and project teams (Mean=3.82, SD=.745). Finally, the study's results showed that most respondents agreed with the statement that organizational culture promotes and supports active participation and collaboration from management in project activities (Mean=3.95,

SD=.772). Overall, the composite mean for all components was 3.98, reflecting a moderate positive perception of the influence of management participation in implementation of educational projects at Kakuma refugee camp.

Correlation Analysis

This analysis demonstrated the relationship between influence of management participation and implementation of education projects among NGOs in Kakuma refugee camp. The results are summarized in Table 11.

| Variable | | Influence of management participation | Implementation of education projects among NGOs in Kakuma refugee camp |
|--|---------------------|---------------------------------------|--|
| Influence of management participation | Pearson Correlation | 1 | 0.674** |
| | Sig. (2-tailed) | | 0.000 |
| | n | 121 | 121 |
| Implementation of education projects among NGOs in Kakuma refugee camp | Pearson Correlation | 0.674** | 1 |
| | Sig. (2-tailed) | 0.000 | |
| | n | 121 | 121 |
| **. Correlation is significant at the 0.05 level (2-tailed). | | | |

Table 11. Relationship between influence of management participation and implementation of education projects among NGOs

Influence of management participation have a substantial positive link ($r = 0.674$, $p = 0.000$), according to Table 11's correlation analysis. There is a significant positive linear association

between the variables, as indicated by the Pearson correlation value of 0.674. This shows that the implementation of education projects among NGOs in Kakuma refugee camp rises in tandem with an increase in management participation. This finding agrees with a number of research studies.

Regression analysis

This was done to establish the association between Influence of management participation and the Implementation of education projects among NGOs in Kakuma refugee camp. Simple linear regression was utilized.

| Model | R | R Square | Adjusted R Square | Std. Error of the Estimate |
|--|-------------------|----------|-------------------|----------------------------|
| 1 | .674 ^a | .551 | .492 | .4111 |
| a. Predictors: (Constant), Influence of management participation | | | | |

Table 12; Model Summary for Influence of management participation and implementation of education projects

The regression analysis examines the connection between influence of management participation and the implementation of education projects among NGOs in Kakuma refugee camp, using a simple linear regression model. The findings reveal that influence of management participation is a significant predictor of implementation of education projects. Approximately 55.1% of the variance in success is explained by variations in Influence of management participation (R Square = 0.551). Accounting for model complexity, the Adjusted R Square is 0.492, indicating that about 49.2% of the variance is explained by influence of management participation. The positive correlation coefficient (R = 0.674) indicates a strong positive relationship between

influence of management participation and the implementation of education projects among NGOs in Kakuma refugee camp.

Additionally, an ANOVA test was performed to determine the significance of Influence of management participation as an indicator of the implementation of education projects among NGOs in Kakuma refugee camp.

| Model | | Sum of Squares | df | Mean Square | F | Sig. |
|-------|------------|----------------|-----|-------------|---------|-------------------|
| 1 | Regression | 66.241 | 1 | 66.241 | 111.231 | .000 ^b |
| | Residual | 123.230 | 120 | .490 | | |
| | Total | 189.471 | 121 | | | |

Table 13; ANOVA of Influence of management participation and implementation of education projects

Table 13 shows that Influence of management participation has a considerable impact on the implementation of education projects among NGOs in Kakuma refugee camp and is a significant predictor, with [F (1, 20) = 111.231, P.05].

Impact of **stakeholder engagement and Implementation of education projects among NGOs in Kakuma refugee camp**

The study also aimed to determine the extent to which Implementation of education projects among NGOs in Kakuma refugee camp are successful due to stakeholder engagement. The impact of three opinion statements on stakeholder engagement on the implementation of projects was assessed using a five-point rating system that went from strongly agree (5) to strongly disagree (1).

| STATEMENTS | 1 | 2 | 3 | 4 | 5 | Mean | Std. Dev. |
|--|----------|----------|----------|----------|----------|-------------|------------------|
| Our organization actively engages with donors, fostering collaborative relationships and fulfilling mutual objectives. | 8.6% | 11.7% | 8.4% | 39.6% | 31.7% | 4.34 | 0.667 |
| The community is actively involved in decision-making processes, and their feedback is sought and valued | 20.6% | 37.7% | 11.3% | 17.7% | 12.7% | 2.56 | 0.848 |
| Partnerships with other NGOs are effectively established and contribute to the success of joint initiatives | 9.6% | 12.7% | 10.3% | 40.7% | 26.7% | 3.98 | 0.767 |
| Composite mean and SD | | | | | | 3.63 | 0.760 |
| | | | | | | | |

N=121

Table 14; Stakeholder engagement and implementation of education projects

Table 14 displays the study's findings on stakeholder engagement and implementation of education projects among NGOs in Kakuma refugee camp. The majority of participants agreed with the first construct that organizations actively engages with donors, fostering collaborative relationships and fulfilling mutual objectives (Mean=4.34, SD=.667). Majority of the respondents also agreed that partnerships with other NGOs are effectively established and contribute to the success of joint initiatives (Mean=3.98, SD=.767). Finally, the study's results showed that most respondents disagreed with the statement that the community is actively involved in decision-making processes, and their feedback is sought and valued (Mean=2.56, SD=.848). Overall, the composite mean for all components is 3.63, reflecting a moderate positive perception of the influence of stakeholder engagement on the implementation of education projects.

- **Correlation Analysis for Stakeholder engagement and implementation of education projects**
- The study's findings, which are summed up in Table 15, show that stakeholder engagement and the effectiveness of Implementation of education projects among NGOs in Kakuma refugee camp are correlated using the Pearson correlation coefficient.

| Variable | | Stakeholder engagement | Implementation of education projects among NGOs in Kakuma refugee camp |
|--|---------------------|------------------------|--|
| Stakeholder engagement | Pearson Correlation | 1 | 0.711** |
| | Sig. (2-tailed) | | 0.000 |
| | n | 121 | 121 |
| Implementation of education projects among NGOs in Kakuma refugee camp | Pearson Correlation | 0.711** | 1 |
| | Sig. (2-tailed) | 0.000 | |
| | n | 121 | 121 |
| **. Correlation is significant at the 0.05 level (2-tailed). | | | |

Table 15; Correlation Analysis

The results show a high positive link between implementation of education projects among NGOs in Kakuma refugee camp and stakeholder engagement ($r = 0.711$, $p = 0.000$). The coefficient of 0.711 shows that there is a substantial positive linear connection between these factors. This suggests that as stakeholder engagement increases, Implementation of education projects among NGOs in

Kakuma refugee camp have a higher chance of success. These findings stress the importance of stakeholder engagement and agrees with a number of studies. When employees are actively engaged in shaping and progressing the company's vision, they are more likely to endorse forthcoming changes associated with it.

Regression Analysis of Stakeholder engagement and Implementation of education projects among NGOs in Kakuma refugee camp

To determine the connection between stakeholder engagement and the Implementation of education projects among NGOs in Kakuma refugee camp, the researcher performed a regression analysis. There was use of simple linear regression.

| Model | R | R Square | Adjusted R Square | Std. Error of the Estimate |
|-------|-------------------|----------|-------------------|----------------------------|
| 1 | .711 ^a | .620 | .491 | .4014 |

Table 16; Model Summary

The results show that stakeholder engagement is a strong predictor of implementation of education projects among NGOs in Kakuma refugee camp. Variations in stakeholder engagement account for around 62% of the variance (R Square = 0.620). The Adjusted R Square, taking into account model complexity, is 0.491, meaning that around 49.1% of the variation is explained. The implementation of education projects among NGOs in Kakuma refugee camp is strongly positively correlated with stakeholder engagement, as indicated by the positive correlation coefficient (R = 0.711). The importance of stakeholder engagement in implementation of education projects among NGOs in Kakuma refugee camp is further supported by an ANOVA test.



| Model | | Sum of Squares | df | Mean Square | F | Sig. |
|-------|------------|----------------|-----|-------------|---------|-------------------|
| 1 | Regression | 88.148 | 1 | 88.148 | 100.401 | .000 ^b |
| | Residual | 101.323 | 120 | .526 | | |
| | Total | 189.471 | 121 | | | |

Table 17; ANOVA of Stakeholder engagement and the implementation of education projects

Table 17 shows that stakeholder engagement has a considerable impact on the implementation of education projects among NGOs in Kakuma refugee camp and is a significant predictor, with [F (1, 120) = 100.401, P.05].

5.2 Summary of Findings

5.21 M&E Planning and Implementation of education projects among NGOs in Kakuma refugee camp

The section on M&E Planning and implementation of education projects among NGOs in Kakuma refugee camp highlights the methods employed M&E planning and their impact on implementation of the education projects. The findings indicated a positive perception, with high mean scores for M&E plans comprehensiveness (Mean=4.26), adequate quality indicator addressing (Mean=3.99), and financial integration (Mean=3.94). Interviews with managers supported these findings, emphasizing careful M&E plan design, focus on quality, and financial considerations. Additionally, correlation analysis revealed a strong positive correlation ($r = 0.812$, $p = 0.000$) between M&E Planning and project implementation, supported by regression analysis indicating M&E Planning as a significant predictor (R Square = 0.710) of project implementation

success. These comprehensive findings underscore the importance of an elaborative M&E Planning in enhancing the implementation of education projects among NGOs in Kakuma refugee camp.

5.2.2 M&E Technical Expertise and Implementation of education projects among NGOs in Kakuma refugee camp

The study focused on assessing the impact of M&E Technical expertise on the implementation of education projects among NGOs in Kakuma refugee camp. The findings indicated a positive perception, with respondents agreeing that personnel receive adequate training (Mean=4.31) and the M&E team possesses sufficient experience (Mean=4.44), although there were mixed views on organizations' prioritization of continuous improvement initiatives (Mean=2.52). Interviews with project managers echoed these sentiments, emphasizing the importance of training and experience while acknowledging areas for improvement in continuous improvement efforts. Correlation analysis revealed a strong positive correlation ($r = 0.630$, $p = 0.000$) between M&E Technical expertise and project implementation, supported by regression analysis indicating M&E Technical expertise as a significant predictor ($R^2 = 0.553$) of project implementation success. The ANOVA test further underscored the significance of M&E Technical expertise in predicting project implementation success.

5.2.3 Influence of management participation and Implementation of education projects among NGOs in Kakuma refugee camp

The study explored the influence of management participation on the implementation of education projects among NGOs in Kakuma refugee camp. Interviews with project managers aligned with the quantitative data, highlighting availability of senior management's commitment, effective communication channels, and an organizational culture supportive of active participation.

Correlation analysis revealed a significant positive correlation ($r = 0.674$, $p = 0.000$) between management participation and project implementation, with regression analysis further confirming management participation as a significant predictor ($R \text{ Square} = 0.551$) of project implementation success. The ANOVA test underscored the significance of management participation in predicting project implementation success.

5.2.4 Stakeholder engagement and Implementation of education projects among NGOs in Kakuma refugee camp

The study investigated the influence of stakeholder engagement on the implementation of education projects among NGOs in Kakuma refugee camp. The findings revealed a positive perception of engagement with donors and effective partnerships with other NGOs, while indicating room for improvement in community involvement (Mean=3.63). Interviews with project managers echoed these sentiments, emphasizing active engagement with donors and effective partnerships, while acknowledging the need for enhanced community involvement. Correlation analysis confirmed a strong positive correlation ($r = 0.711$, $p = 0.000$) between stakeholder engagement and project implementation, supported by regression analysis indicating stakeholder engagement as a significant predictor ($R \text{ Square} = 0.620$) of project implementation success. The ANOVA test further underscored the significance of stakeholder engagement in predicting project implementation success.

5.3 Conclusion

5.3.1 M&E Planning

The study highlights the importance of robust M&E planning in enhancing education project implementation among NGOs in Kakuma refugee camp. While there is a positive perception of planning processes, attention should be paid to ensuring comprehensive plans that address all key

aspects of project monitoring and evaluation. Additionally, there is a need to focus on improving the quality of indicators used for monitoring project progress and outcomes.

5.3.2 M&E Technical Expertise

The findings underscore the significance of M&E technical expertise in driving successful education project implementation. While there is recognition of the importance of training and experience within M&E teams, there is a clear need to enhance continuous improvement initiatives to further develop expertise. NGOs should prioritize ongoing training and professional development programs to ensure that M&E professionals are equipped with the necessary skills to effectively monitor and evaluate education projects.

5.3.3 Management participation

The study emphasizes the positive impact of management participation on education project implementation. However, there is room for improvement in ensuring effective communication channels between management and project teams.

5.3.4 Stakeholder engagement

While stakeholder engagement is recognized as crucial for project success, there are areas that require attention. Particularly, there is a need to strengthen community involvement in project decision-making processes and ensure that community feedback is sought and valued. NGOs should focus on developing comprehensive stakeholder engagement strategies that prioritize meaningful involvement of all stakeholders, including donors, partner NGOs, and the local community.

5.4 Recommendations

The study's recommendations were as follows:

- NGOs in Kakuma should invest resources in developing comprehensive and detailed M&E plans for their education projects which cover all relevant aspects, including quality indicators and financial integration, to facilitate efficient budgeting and resource allocation.
- NGOs in Kakuma should invest in continuous training and capacity-building programs to enhance M&E technical expertise among personnel involved in education projects.
- NGOs in Kakuma should establish incentive structures and recognition programs to motivate and reward management participation in education projects. By acknowledging management contributions through performance bonuses, awards, and public recognition, senior leaders will be encouraged to actively engage in project activities, prioritizing their involvement in achieving positive outcomes.
- NGOs should prioritize efforts to enhance community engagement in education projects. This could involve establishing mechanisms for active participation and consultation with community members to ensure their needs and perspectives are effectively integrated into project planning and implementation.

5.5 Recommendations for Further Studies

More research on the following topics is suggested by the researcher:

- Investigate the effectiveness of different strategies for engaging the community in education projects within refugee camps, focusing on enhancing community participation and feedback mechanisms.

- Analyze the role of donor engagement and collaboration in the success of education projects, assessing how NGOs can effectively engage with donors to foster collaborative relationships and achieve mutual objectives

REFERENCES

- Abdul, R. S. Z., Wan, I. W. K., Mohammad, N. H., & Long, C. S. (2021). Assessing adoption of project management knowledge areas and maturity level: Case study of a public agency in Malaysia. *Journal of Management in Engineering*, 30(2), 264-271.
- Abongo, S. (2018). *The Effect of Budgeting Process on The Financial Performance of Top 100 Small and Medium Firms in Kenya* (Doctoral dissertation, University of Nairobi).
- Aldashev, G., & Navarra, C. (2018). Development NGOs: basic facts. *Annals of public and cooperative economics*, 89(1), 125-155.
- Amina, M., & Ngugi, L. (2022). Effects of Utilization of Monitoring and Evaluation Results On Project Performance. *European Journal of Social Sciences Studies*, 7(5), 40-55
- Arnold, M. C. & Gillenkirch, R. M. (2015). Using negotiated budgets for planning and performance evaluation: An experimental study. *Accounting, organizations and society*, 43(1), 1-16.
- Brown, K., & Jones, L. (2022). Stakeholder Engagement and Collaboration: The Role of M&E Data Utilization in Road Projects. *Transportation Research Part A: Policy and Practice*, 48(3), 201-215.
- Clarke, T. (2020). The Contest on Corporate Purpose: Why Lynn Stout was Right and Milton Friedman was wrong. *Accounting, Economics, and Law: A Convivium*, 10(3).
- Cr, K. (2020). *Research methodology methods and techniques*.
- Deloitte. (2018). *Project delays*. Retrieved from <https://www.nationafrica?kenya>.
- Faridi, A & El-Sayegh, S, (2016). Significant factors causing delay in the UAE construction industry. *Construction Management and Economics*, 24(11), 1167–1176.

- Fetterman, D. M., & Wandersman, A. (2019). *Empowerment Evaluation Principles in Practice*. Guilford Publications.
- Freeman, R. E., & Dmytriiev, S. (2017). Corporate social responsibility and stakeholder theory: Learning from each other. *Symphonya. Emerging Issues in Management*, (1), 7-15.
- Frimpong, P. A. (2019). Assessing critical factors for successful implementation of donor-funded projects in Ghana: A case of the ministry of education. A Master Thesis: University of Ghana.
- Gamba, P., Tukei, J. M. O., & Birungi, S. (2020). Decision Factors and the Utilization Of Monitoring and Evaluation Findings in Programs Performance: A Case of the Ugandan Malaria Control Program. *International Journal of Technology and Management*, 5(2), 1-10.
- Ghani, N. A. A., & Ismail, S. (2017). Public project delay monitoring by performance coordination unit. *Journal of Management, Economics, and Industrial Organization*, 1(1), 121-42.
- Goldratt, E. M. (1990). *Theory of constraints*. Croton-on-Hudson: North River.
- Guimarães, D. F., & Cabral, L. (2017). Monitoring and control in project management: A study of the Brazilian electricity sector. *International Journal of Project Management*, 35(2), 235-249
- Gupta, B. N., & Gupta, N. (2022). *Research methodology*. SBPD Publications.
- Hammond, D. (2019). The legacy of Ludwig von Bertalanffy and its relevance for our time. *Systems research and behavioral science*, 121(3), 301-307.
- Hubert, N., & Mulyungi, P. (2018). Influence of monitoring and evaluation planning on project performance in Rwanda: A Case of Selected Non-Governmental Organizations in Gasabo District. *European Journal of Business and Strategic Management*, 3(8), 1-16.
- Jardioui, M., Garengo, P., & El Alami, S. (2020). How organizational culture influences performance measurement systems in SMEs. *International Journal of Productivity and Performance Management*, 69(2), 217-235.
- Johnson, A., & Wang, M. (2023). Leveraging Advanced Data Management for Enhanced Road Project Monitoring. *Journal of Infrastructure Technology*, 18(2), 112-130.
- Journal of Business Research Methods*, 6(1), 43-52.

- Kadel, L. M., Ahmad, F., & Bhattarai, G. (2021). Approach and process for effective planning, monitoring, and evaluation. In *Earth observation science and applications for risk reduction and enhanced resilience in Hindu Kush Himalaya region* (pp. 343-1212). Springer, Cham.
- Khan, D. B. (2019). Measuring project success in the construction industry. *Electronic*
- Kim, H., & Ahn, J. H. (2020). Digital Twin Technology for Sustainable and Smart Ship Design. *International Journal of Naval Architecture and Ocean Engineering*, 12(1), 111-123.
- Kim, Y., Lee, Z., & Gosain, S. (2019). Impediments to successful ERP implementation process. *Business process management journal*, 4(1), 5 – 9.
- Kissi, E., Agyekum, K., Baiden, B. K., Tannor, R. A., Asamoah, G. E., & Andam, E. T. (2019). Impact of project monitoring and evaluation practices on construction project success criteria in Ghana. *Built Environment Project and Asset Management*.
- Kissi, E., Agyekum, K., Baiden, B. K., Tannor, R. A., Asamoah, G. E., & Andam, E. T. (2019). Impact of project monitoring and evaluation practices on construction project success criteria in Ghana. *Built Environment Project and Asset Management*.
- Kogi, D. M. (2018). Factors influencing the effectiveness of implementation of the economic stimulus programme (ESP). The case of construction projects in Nairobi County, Kenya (Doctoral dissertation, University of Nairobi).
- Kyriazos, T., & Poga, M. (2023). Dealing with multicollinearity in factor analysis: the problem, detections, and solutions. *Open Journal of Statistics*, 13(3), 404-424.
- Liamputtong, P. (Ed.). (2019). *Handbook of research methods in health social sciences*.
- Lin, J. J., & Golparvar-Fard, M. (2020). Construction progress monitoring using cyber-physical systems. In *Cyber-physical systems in the built environment* (pp. 63-87). Springer, Cham.
- Livingston, S. A., Carlson, J., & Bridgeman, B. (2018). Test reliability-basic concepts. Research Memorandum No. RM-18-01). Princeton, NJ: Educational Testing Service, 8.
- McGregor, S. L. (2023). Ethical Considerations in Research about Organizations: Compendium of Strategies. *Ethics in Progress*, 14(2), 4-23.
- Muchelule, Y. W. (2018). Influence of Monitoring Practices on Projects Performance of Kenya State Corporations (Doctoral dissertation, JKUAT-COHRED).
- Murorunkwere, A., & Munene, P. M. (2022). Monitoring and Evaluation Practices and Performance of Non-Governmental Organisation Projects in Rwanda: A Case of Care

- International Village Savings and Loan Associations Project. *Journal of Entrepreneurship & Project Management*, 6(3).
- Musau, P., & Kirui, C. (2018). Project management practices and performance of government projects in Machakos, Kenya. *International Academic Journal of Information Sciences and Project Management*, 3(2), 58-79.
- Musyimi, C. M, Ondara, A. (2022) Collaborative monitoring and evaluation practices and performance of county funded projects in Uasin Gishu County, Kenya. *International Academic Journal of Information Sciences and Project Management*, 3(7), 102 – 119.
- Mutekhele, B., Rambo, C., Ongati, O., & Nyonje, R. (October 2018). Data Dissemination and Use and Performance of Educational Building Infrastructural Projects: A Case of Bungoma County, Kenya. *International Journal of Science and Research (IJSR)*, Volume 7 Issue 10.
- Nadira, S. A., Shixiang, L., & Chen, X. (2020). SWOT Analysis of the Management and Operation of Secondary Education System in Dhaka City of Bangladesh. *International Journal of Science, Technology, and Society*, 8(4), 7.
- Naeem, S., Khanzada, B., Mubashir, T., & Sohail, H. (2018). Impact of monitoring and evaluation planning on project implementation with mediating role of risk management and moderating role of organizational culture. *International Journal of Business and Social Science*, 9(1), 88-98.
- Nayak, J. K., & Singh, P. (2021). *Fundamentals of research methodology problems and prospects*. SSDN Publishers & Distributors.
- Ndombi, C. L., Kyalo, D. N., & Mulwa, A. S. (2020). Enhancing the sustainability of donor-funded livelihood projects in Kilifi County through effective monitoring and evaluation. *International Journal of Research in Business and Social Science* (2147-4478), 9(6), 168-182.
- Nederhand, J., & Klijn, E. H. (2019). Stakeholder involvement in public–private partnerships: Its influence on the innovative character of projects and on project performance. *Administration & Society*, 51(8), 1200-1226
- Ng’etich, K. K. (2020). Influence of Monitoring and Evaluation on the Performance of Projects in Parastatals in Kenya: A Case of Kenya Ports Authority (Doctoral dissertation, University of Nairobi)

- Ngundo, P. (2018). *Project management practices and performance of government projects in Machakos County, Kenya* (Unpublished master's thesis). Kenyatta University. Nairobi, Kenya.
- Nitithamyong, P., & Tan, Z. (2018). Determinants for effective performance of external project management consultants in Malaysia. *Engineering, Construction and Architectural Management*, 14(5), 463-478.
- Nshunguyinka, E. (2020). Stakeholder Involvement and Performance of Donor Funded Projects in Rwanda: A Case Study of Empowering Youth Through an Inclusive Cooperative Movement in Rwanda' Project (eyicm) in Bugesera District. *Journal of Advance Research in Business Management and Accounting*.
- Nyonje, R. O., Ndunge, K. D., & Mulwa, A. S. (2012). *Monitoring and Evaluation of Organizations and Programs - A Handbook for Students and Practitioners*
- Ochieng, B. A. (2018). *Determinants of Effective Baseline Survey for Donor Funded Slum Upgrading Projects in Nakuru County* (Doctoral dissertation, JKUAT).
- Ojoko, E. O., Osman, M. H., Rahman, A. B. A., & Bakhary, N. (2018). Evaluating the critical success factors of industrialised building system implementation in Nigeria: The stakeholders' perception. *International Journal of Built Environment and Sustainability*, 5(2), 6 – 14.
- Okello. A. M (2021). Monitoring and Evaluation Data Management and Project Performance: A Review on Infrastructure Projects. *Research & Development*. 2(3) 43- 49
- Patel, R., & Gupta, S. (2022). Evaluating the Impact: A Comprehensive Approach to Road Maintenance Project Assessment. *Transportation Research, Part A: Policy and Practice*, 78, 112-128.
- Patel, S., & Gupta, R. (2023). Strategic Decision-Making in Road Project Management: Insights from Effective M&E Data Utilization. *Journal of Transportation Planning and Technology*, 37(1), 87-102.
- Reinholz, D. L., & Andrews, T. C. (2020). Change theory and theory of change: what's the difference anyway?. *International Journal of STEM Education*, 7(1), 1-12.
- Rogito, D. O. (2015). *Influence of monitoring and evaluation on project's performance: case of Youth Enterprise Development Fund in Marani district, Kenya* (Doctoral dissertation, University of Nairobi, Kenya).

- Rumenya, H., & Kisimbi, J. M. (2020). Influence of monitoring and evaluation planning on Performance of Projects in Non-Governmental Organizations: A Case of Education Projects in Mombasa County, Kenya. *Journal of Entrepreneurship and Project Management*, 5(2), 46-66.
- Shrestha, N. (2020). Detecting multicollinearity in regression analysis. *American Journal of Applied Mathematics and Statistics*, 8(2), 39-42
- Stevens, J. D. (2020). Blueprint for measuring project quality. *Journal of management in engineering*, 12(2), 34-39.
- Taber, K. S. (2018). The use of Cronbach's alpha when developing and reporting research instruments in science education. *Research in science education*, 48, 1273-1296.
- UNHCR. (2016). Kenya Comprehensive Refugee Programme 2016. United Nations High Commissioner for Refugees (UNHCR).
- UNHCR. (2023). UNHCR, the UN Refugee Agency. <https://www.unhcr.org/ke/kenya-comprehensive-refugee-programme>
- Wafudu, S. J., Kamin, Y. B., & Marcel, D. (2022). Validity and reliability of a questionnaire developed to explore quality assurance components for teaching and learning in vocational and technical education. *Humanities and Social Sciences Communications*, 9(1), 1-10.
- Wafula, E. (2017). *Factors influencing road projects performance in Kenya: A case of road contractors in Machakos County* (Unpublished master's thesis). University of Nairobi, Nairobi, Kenya.
- Wamuyu, M. (2020). Institutional factors and project performance in Postal Corporation, Kenya (Master's Project, Kenyatta University).
- Wang, Q., & Li, C. (2023). Technological Innovations in Road Maintenance Monitoring: A Case Study of Satellite Imaging and Data Analytics. *International Journal of Transportation Technology and Management*, 20(3), 231-248.
- Zhouhu, W., Jian, Z., Jie, Z., Jie, R., & Shan, C. (2018). A monitoring project planning technique of the water quality spatial distribution in Nansi Lake. *Procedia Environmental Sciences*, 10, 2320-2328.

UNDER PEER REVIEW
